




**ACTIVE PROJECTS BY THE NUMBERS**


**ACTIVE PROJECT STATUSES**

- **Planning** - Project plans are documented, the project deliverables and requirements are defined with stakeholders and reviewing agencies, and the project schedule is created.
- **Scope Development** - A comprehensive scope suitable for design or design-build procurement is being developed for the approved project.
- **Design Procurement** - Services are being solicited for architectural/engineering services to complete design documents.
- **Design** - Project is being designed by the Architect/Engineer and going through the necessary review & approval processes.
- **Contractor Procurement** - Construction services are being solicited.
- **In Construction** - The construction work is awarded to a Contractor and preconstruction (e.g., material ordering) and/or active construction is underway.
- **Substantial Completion** - Construction work is sufficiently completed with all requisite inspections & approvals obtained for use and/or occupancy.
- **Final Completion (Closeout Approval Requested)** - Project manager has fully accepted contract work AND punchlist/corrective work is 100% complete; any required trade permits/inspections are 100% approved; applicable operating manuals, as-builts & warranty information are on hand; and, final payment is approved.

Active Projects By Status	#
Planning	34
Scope Development	13
Design Procurement	2
Design	26
Contractor Procurement	40
In Construction	39
Substantially Complete	82
Final Completion (Closeout Approval Requested)	147
<b>TOTAL ACTIVE PROJECTS</b>	<b>383</b>

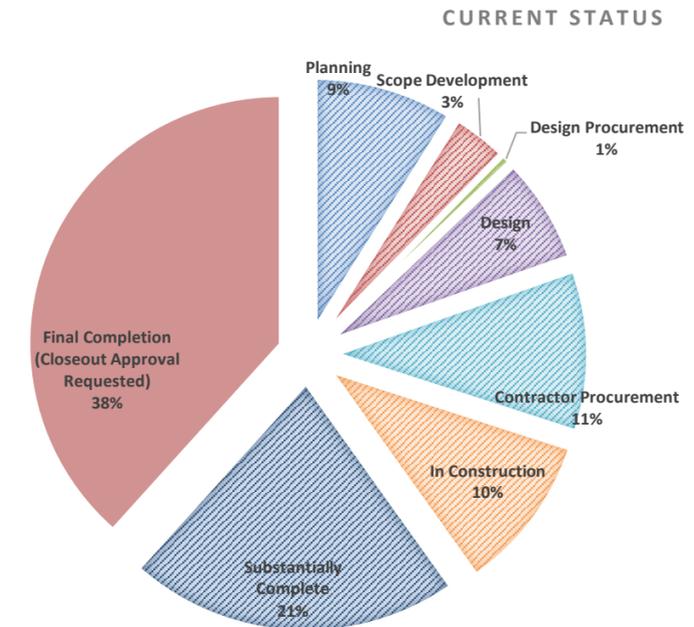

Active Projects By Type	#	Funding
Abatement	20	\$ 5,303,777.00
ADA Upgrades	7	\$ 1,737,977.00
Athletic Improvements	15	\$ 27,125,861.00
Building Repairs: Major/Emergency	8	\$ 13,957,141.01
Building Repairs: Minor	24	\$ 5,239,547.48
Central Garage & Transportation	3	\$ 535,700.00
Code Corrections	47	\$ 4,509,190.37
Emergency / Major Repair	0	\$ -
Exterior Door/Window Upgrades	15	\$ 20,087,657.58
IT Upgrades	4	\$ 102,631.50
Kitchen & Food Services	25	\$ 8,397,000.00
New Schools & Modernizations	17	\$ 670,722,865.00
Other	13	\$ 590,800.00
Parking Lots	11	\$ 4,008,000.00
Playgrounds	4	\$ 1,501,275.12
Renovations: Career Academy	11	\$ 18,512,000.00
Renovations: Classroom	2	\$ -
Renovations: Misc	8	\$ 28,984,859.00
Renovations: Staged	0	\$ -
Renovations: Pod Conversions	6	\$ 17,006,000.00
Security Upgrades	43	\$ 7,989,307.64
Systemic Upgrades: Electrical	4	\$ 7,126,222.00
Systemic Upgrades: HVAC	66	\$ 198,208,883.98
Systemic Upgrades: Life-Safety	4	\$ 620,000.00
Systemic Upgrades: Misc	26	\$ 55,831,340.00
<b>TOTAL</b>	<b>383</b>	<b>\$ 1,098,098,035.68</b>

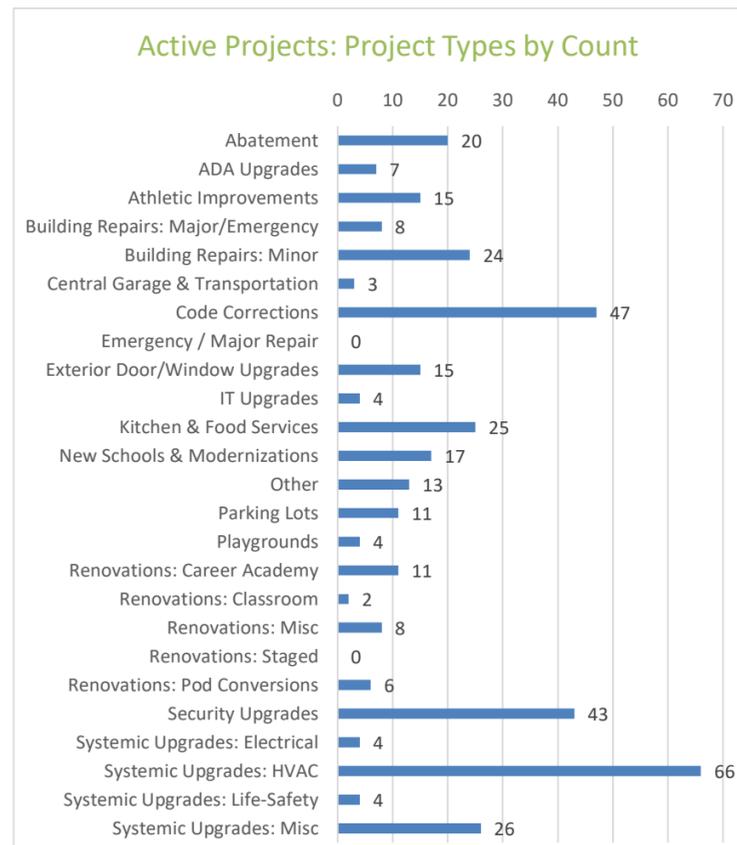

**Prince George's County Public Schools**  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
**January 2026**

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Allenwood ES	FY/17	State & County Funded	\$575,000	Exterior Door/Window Upgrades	Courtyard Windows Wall Replacement. A total of 49 windows and 7 doors will be replaced.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	08/13/18	02/22/19	100%
7	Andrew Jackson Academy	FY/18	State & County Funded	\$17,641,000	Systemic Upgrades: HVAC	Replace 1971 HVAC equipment including one (1) chiller, 14 air handling units, heating and cooling piping, and the controls system, replace one (1) 1996 cooling tower, and replace two (2) 2000 steam boilers with hot water boilers.	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	09/14/20	07/03/23	99%
7	Andrew Jackson Academy	FY/18	State & County Funded	\$639,000	Exterior Door/Window Upgrades	Window Replacement - All exterior windows throughout the building. The work consists of demolishing existing window system, removal of all related debris, and installation of 85 commercial grade aluminum single hung insulated window units	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	09/01/20	08/20/22	99%
7	Andrew Jackson Academy	FY/21	County Funded	\$227,218	Security Upgrades	Install, program and test One hundred Eight IP Network Cameras (31- Outside, 77- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	04/16/21	06/30/21	
4	Annapolis Road Academy	FY/16	State & County Funded	\$890,000	Systemic Upgrades: HVAC	Steam and Condensate Piping Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
4	Annapolis Road Academy	FY/16	State & County Funded	\$255,000	Systemic Upgrades: HVAC	Roof Top Unit Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
4	Annapolis Road Academy	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Substantially Complete	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/07/21	08/26/22	99%
8	Apple Grove ES	FY/22	County Funded	\$692,000	Systemic Upgrades: Misc	Roofing Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	08/25/23	08/03/24	100%
8	Apple Grove ES	FY/24	County Funded	\$250,000	Abatement	Asbestos Abatement	In Construction	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/10/24		
8	Apple Grove ES	FY/26	State & County Funded	\$2,357,000	Exterior Door/Window Upgrades	Replace the 1967 and 1998 windows and doors.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
8	Apple Grove ES	FY/26	County Funded	\$189,600	Code Corrections	Fire Alarm System Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
4	Ardmore ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	02/15/17	100%
4	Ardmore ES	FY/26	County Funded	\$11,353	Building Repairs: Minor	Multipurpose Room Stage Flooring Refurbishment	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
9	Baden ES	FY/14	State & County Funded	\$1,144,450	Systemic Upgrades: HVAC	Air Conditioning Initiative (ACI) - The request is to install a central air conditioning in the 1967 school building.	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	06/14/17	09/29/17	99%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Baden ES	FY/17	State & County Funded	\$129,000	Exterior Door/Window Upgrades	Exterior Doors Replacement	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>		03/01/19	99%
4	Beacon Heights ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/20/21	100%
4	Beacon Heights ES	FY/17	State & County Funded	\$4,473,000	Systemic Upgrades: HVAC	AHUs, Condensate Piping, Metal Pan Ceiling & Univents Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/17/19	08/21/19	95%
4	Beacon Heights ES	FY/26	State & County Funded	\$2,143,000	Systemic Upgrades: Misc	Replace the 1998 39,825 sf built-up roof.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
4	Beacon Heights ES	FY/26	County Funded	\$175,000	Code Corrections	Fire Alarm System Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
1	Beltsville Academy	FY/17	State & County Funded	\$2,811,000	Systemic Upgrades: HVAC	Univents & Controls and Window Replacement: 270 windows including tech fab panels will be replaced.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	01/31/19	09/01/19	100%
1	Beltsville Academy	FY/18	State & County Funded	\$2,453,000	Systemic Upgrades: Misc	Roof Replacement - replace the entire 84,169 sf - 1991 built-up roof and 173 sf 1991 metal roof, including soffit and fascia at the music wing.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/20/19	09/01/19	100%
1	Beltsville Academy	FY/24	Operating Funds	\$300,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/10/24		
1	Beltsville Academy		County Funded	\$2,341,310	Renovations: Misc	Provide (10) classroom modular additions	In Construction	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	09/01/22	08/15/23	100%
7	Benjamin Foulois K8	FY/23	Operating Funds	\$405,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	<a href="mailto:garth.deitzer@pgcps.org">garth.deitzer@pgcps.org</a>			
4	Benjamin Stoddert MS	FY/23	County Funded	\$800,000	Kitchen & Food Services	Kitchen Renovation	Substantially Complete	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>			94%
5	Benjamin Tasker MS	FY/15	County Funded	\$60,000	Systemic Upgrades: Life-Safety	Code Corrections Fire Hydrant Project - This project consists of the replacement of the existing Fire Alarm System to meet current County, State and Federal building codes	Design Procurement	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/17	09/30/17	0%
5	Benjamin Tasker MS	FY/17	State & County Funded	\$1,150,000	Systemic Upgrades: HVAC	Piping Replacement & Insulation: includes removal and replacement of all existing piping, steam traps and hangers on the dual distribution system. This will be Phase 1, which will consist of half of the school.	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/20/19	01/31/20	100%
5	Benjamin Tasker MS	FY/19	County Funded	\$216,524	Security Upgrades	Provide and install the following: 1. (98) Ninety-eight IP Network Cameras (24- Outside, 74- Inside) 2. 160TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC with a 22" Monit	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	06/17/19	08/16/19	100%
5	Benjamin Tasker MS	FY/25	Grant Funded-ESSER	\$10,979,371	Renovations: Misc	Modular Addition	In Construction	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>		02/02/26	13%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Berwyn Heights ES	FY/19	County Funded	\$107,444	Security Upgrades	Provide and install the following: 1. (41) Forty-nine IP Network Cameras (15- Outside, 26- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	07/08/19	11/30/19	100%
2	Berwyn Heights ES	FY/20	County Funded	\$2,000,000	Renovations: Misc	A phased limited renovation (Staged Renovation) of the facility.	Planning	<a href="mailto:ronald.skyles@pgcps.org">ronald.skyles@pgcps.org</a>			
4	Bladensburg ES	FY/16	County Funded	\$50,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is to be performed within the kitchen renovation project that is unable to be performed due to contractor's non-performance.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	08/28/18	09/14/18	99%
4	Bladensburg ES	FY/16	County Funded	\$550,000	Kitchen & Food Services	Kitchen Renovation - This project includes the disconnection, removal, and dispose of the kitchen breaker panel (see note below), dishwasher, tables, dishwasher hood, booster heater, dish window, serving line, dish room wall, existing kitchen exhaust hood	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	04/16/18	08/23/19	99%
4	Bladensburg ES	FY/19	County Funded	\$119,820	Security Upgrades	Provide and install the following: 1. (49) Forty-nine IP Network Cameras (17- Outside, 32- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC wit	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	06/03/19	07/19/19	100%
4	Bladensburg ES	FY/22	County Funded	\$3,305,513	Systemic Upgrades: HVAC	HVAC and Total Roof	Scope Development	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>			0%
4	Bladensburg ES	FY/22	County Funded	\$3,618,000	Systemic Upgrades: Misc	Roofing Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	04/09/24	06/04/24	100%
4	Bladensburg HS	FY/15	County Funded	\$4,140,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academies of Consumer Services Hospitality & Tourism and Health & Biosciences	Substantially Complete	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	04/06/20	09/14/22	98%
4	Bladensburg HS	FY/15	County Funded	\$3,026,845	Systemic Upgrades: HVAC	HVAC Replacement Phase 2 (chiller)	Substantially Complete	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	07/01/18	04/15/19	98%
4	Bladensburg HS	FY/20	County Funded	\$5,300,000	Athletic Improvements	New Turf, Lighting and Running Track	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	02/02/23	02/01/24	98%
4	Bonnie F. Johns Media Center	FY/21	County Funded	\$255,616	Security Upgrades	SANS server to for sixty-five IP camera systems located throughout the county.	In Construction	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/15/21	04/30/21	
5	Bowie HS	FY/15	County Funded	\$135,000	ADA Upgrades	Misc. ADA Improvements	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	06/24/15	08/15/16	98%
5	Bowie HS	FY/17	State & County Funded	\$2,556,000	Abatement	Fireproofing for Air Conditioning Piping Replacement: includes the removal of asbestos containing encapsulated sprayed applied fireproofing, pipe insulation and associated mudded fittings.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/27/18	09/03/18	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
5	Bowie HS	FY/22	County Funded	\$54,000	Systemic Upgrades: Misc	Roof Replacement	Planning	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>			
5	Bowie HS	FY/25	County Funded	\$34,240	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	09/20/25	11/14/25	100%
5	Bowie HS Annex	FY/16	State & County Funded	\$25,865,000	New Schools & Modernizations	Limited Renovation - Limited renovation and improvements to the existing special education program. Includes five major systemic projects in addition to selected educational program enhancements and systemic renovations.	In Construction	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	12/19/19	04/29/22	97%
5	Bowie HS Annex	FY/18	County Funded	\$450,000	Kitchen & Food Services	Replace kitchen exhaust system. Create opening in exterior wall for combination walk-in refrigerator and freezer. Provide and install one double convection oven, one two compartment steamer.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/16/19	08/16/19	100%
5	Bowie HS Annex	FY/26	TBD (currently tracking for other programs)		Systemic Upgrades: Misc	Roof Repair (This project has been entered into QB for tracking under the 2026 Facilities Improvement Summer Program. Limited details are currently available. Please contact the assigned PM for additional information.)	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
7	Bradbury Heights ES	FY/17	State & County Funded	\$1,719,000	Systemic Upgrades: Misc	Roof Replacement: includes replacing 50,025 sq. ft. of roof.	Final Completion (Closeout Approval Requested)	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	07/09/18	10/05/18	100%
7	Bradbury Heights ES	FY/26	County Funded	\$400,000	Systemic Upgrades: Life-Safety	Structural Concern - Retaining Wall	Scope Development	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
3	Buck Lodge MS	FY/16	State & County Funded	\$2,186,000	Systemic Upgrades: HVAC	Unit Ventilator and Exhaust Fans Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
3	Buck Lodge MS	FY/19	County Funded	\$198,700	Security Upgrades	Provide and install the following: 1. (87) Eighty-seven IP Network Cameras (23- Outside, 64- Inside) 2. 130TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	06/03/19	07/15/19	100%
3	Buck Lodge MS	FY/24	County Funded	\$35,660	Building Repairs: Minor	Gym - Flooring Refurbishment	Substantially Complete	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	07/24/24		95%
3	Buck Lodge MS	FY/24	County Funded		Building Repairs: Minor	Locker Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_keelan.hendricks@pgcps.org">pg_keelan.hendricks@pgcps.org</a>	06/18/24	08/27/24	100%
5	C. Elizabeth Reig Special Center	FY/16	State & County Funded	\$8,752,876	New Schools & Modernizations	Limited Renovation - Limited renovation and improvements to the existing special education program. Includes five major systemic projects in addition to selected educational program enhancements and systemic renovations.	Substantially Complete	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	12/19/19	10/03/23	98%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	Calverton ES	FY/12	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation - Expand kitchen to allow installation of one additional serving line, walk-in freezer and walk-in refrigerator. Replace kitchen exhaust system. Install elevator to deliver food to the second floor.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/19/17	08/01/17	100%
1	Calverton ES	FY/20	County Funded		New Schools & Modernizations	Phased limited renovation (Staged Renovation) of the facility including an addition	Design	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
6	Capitol Heights ES	FY/22	County Funded	\$478,308	Systemic Upgrades: HVAC	Chiller Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	01/20/24	08/30/24	100%
6	Capitol Heights ES	FY/23	County Funded	\$400,000	Kitchen & Food Services	Kitchen & Food Services Renovation	Design	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/29/26		
6	Capitol Heights ES	FY/26	County Funded		Abatement	Asbestos Removal	Final Completion (Closeout Approval Requested)	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	08/13/25	10/21/25	100%
6	Capitol Heights ES	FY/26	County Funded		Abatement	Asbestos - Reinstall Flooring	Final Completion (Closeout Approval Requested)	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	08/28/25	10/21/25	100%
6	Carmody Hills ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	01/27/17	99%
6	Carmody Hills ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
3	Carole Highlands ES	FY/20	County Funded	\$114,527	Security Upgrades	Provide and install the following: 1. (43) Forty-nine IP Network Cameras (19- Outside, 24- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	08/03/20	08/31/20	100%
3	Carole Highlands ES	FY/23	County Funded	\$675,469	Systemic Upgrades: Misc	Partial Roof Replacement	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	05/15/25	09/30/25	100%
3	Carole Highlands ES	FY/24	State-HSFF Funded	\$2,415,750	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	05/15/25	09/30/25	100%
2	Carrollton ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/12/16	99%
1	Catherine T. Reed ES	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	Catherine T. Reed ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/10/24		
6	Central HS	FY/18	State & County Funded	\$20,218,000	Systemic Upgrades: HVAC	Replace the entire 1982 heating and ventilating system with a complete heating, ventilating and air conditioning system, including boilers, chiller, rooftop units, air handling units, terminal units, piping, and controls.	Substantially Complete	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>	06/24/22	08/26/22	99%
3	Cesar Chavez ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
3	Cesar Chavez ES	FY/21	County Funded	\$444,557	Systemic Upgrades: HVAC	Boilers, 2-MPR AHUs, Water Heater, Controls in Plant Replacement	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	10/01/23	08/16/24	98%
3	Cesar Chavez ES	FY/23	County Funded	\$434,134	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	11/01/24	01/31/25	98%
2	Charles Carroll MS	FY/19	County Funded	\$50,000	Kitchen & Food Services	Remove and Replace (2) New Serving Lines	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%
4	Charles Herbert Flowers HS	FY/15	County Funded	\$199,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academies of Science & Technology and Engineering & Science	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	06/15/17	08/10/17	98%
4	Charles Herbert Flowers HS	FY/16	County Funded	\$38,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Business and Finance.	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	06/15/17	08/10/17	98%
4	Charles Herbert Flowers HS	FY/19	County Funded	\$439,153	Security Upgrades	Provide and install the following: 1. (214) Two Hundred and Fourteen IP Network Cameras (38- Outside, 176- Inside) 2. (2) 160TB Storage Servers RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	01/01/20	04/01/20	100%
4	Charles Herbert Flowers HS	FY/19	County Funded	\$75,000	Kitchen & Food Services	Remove and Replace (3) New Serving Lines	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%
4	Charles Herbert Flowers HS	FY/21	State & County Funded	\$11,168,241	Systemic Upgrades: HVAC	Partial funding to replace the 1999 HVAC system and roof replacement.	In Construction	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	12/23/24		65%
4	Charles Herbert Flowers HS	FY/23	State & County Funded	\$12,483,000	Systemic Upgrades: HVAC	HVAC-Roof Replacement	In Construction	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>			
4	Charles Herbert Flowers HS	FY/25	State-HSFF Funded	\$2,905,391	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Scope Development	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>			
4	Charles Herbert Flowers HS	FY/26	County Funded	\$1,500,000	Systemic Upgrades: HVAC	Three (3) chillers, two (2) air cooled condensers, and cooling tower replacement	Scope Development	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/22/26	08/14/26	
4	Charles Herbert Flowers HS	FY/26	County Funded	\$500,000	Systemic Upgrades: HVAC	Boiler Modernization	Scope Development	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/22/26	08/14/26	
3	Cherokee Lane ES	FY/20	State & County Funded	\$64,375,255	New Schools & Modernizations	Replacement facility to be co-located on Buck Lodge MS site. Expansion from 400 to 800 seats to relieve over enrollment in the Adelphi Area.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	08/03/20	04/15/22	99%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Chillum ES	FY/20	State & County Funded	\$2,558,000	Renovations: Pod Conversions	Convert existing open space pods into conventional classrooms.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/01/22	09/01/23	100%
3	Chillum ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
3	Chillum ES	FY/26	State & County Funded	\$2,596,000	Exterior Door/Window Upgrades	Replace the 1978 windows and exterior doors.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
9	Clinton Grove ES	FY/24	County Funded	\$275,000	Code Corrections	Fire Alarm System Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/30/25	01/14/26	100%
9	Clinton Grove ES	FY/26	County Funded	\$777,000	Systemic Upgrades: Electrical	Switchgear Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
8	Colin L. Powell Academy	FY/26	TBD (currently tracking for other programs)		Other	Major Maintenance Repairs for P3 Schools – Summer 2026  This entry is to track facilities that will be unavailable during Summer 2026 activities due to scheduled maintenance and repairs.	Planning				
4	Columbia Park ES	FY/17	State & County Funded	\$592,000	Systemic Upgrades: HVAC	Univent Replacement: Along with steam heat unit ventilators conversion.	Final Completion (Closeout Approval Requested)	<a href="mailto:kmuse@pgcps.org">kmuse@pgcps.org</a>	06/14/19	01/31/22	100%
6	Concord ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP camera system	Design	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
3	Cool Spring ES	FY/24	State & County Funded	\$95,774,000	New Schools & Modernizations	Construction of a new school in front of the existing Cool Spring Elementary School while the existing school is in operation. The proposed school, including the Judy Center is anticipated to be three floors and accommodate 900 students. The new school will be built to be energy efficient and meet all current building and accessibility codes.	Design	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>			0%
4	Cooper Lane ES	FY/26	State & County Funded	\$1,774,000	Exterior Door/Window Upgrades	Replace the 1962/1963/1966/1993 windows and exterior doors	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
6	Cora L. Rice ES	FY/24	State-ASP Funded	\$335,000	Building Repairs: Minor	Public Address System and Clocks Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	08/16/24	100%
6	Cora L. Rice ES	FY/26	County Funded	\$262,942	Systemic Upgrades: Electrical	PA System - Wiring and Speaker Replacement	In Construction	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	02/02/26	08/14/26	

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Crossland HS	FY/16	County Funded	\$27,553	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/17/19	08/16/19	100%
8	Crossland HS	FY/19	County Funded	\$75,000	Kitchen & Food Services	Remove and Replace (3) New Serving Lines	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%
8	Crossland HS	FY/23	State-ASP Funded	\$2,641,399	Athletic Improvements	Bleacher/Press-Box Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	05/20/24	09/11/24	100%
8	Crossland HS	FY/24	County Funded	\$192,263	Building Repairs: Minor	Gym - Flooring Replacement	Substantially Complete	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	05/29/24		100%
8	Crossland HS	FY/25	County Funded	\$763,000	Athletic Improvements	Stadium Lighting Installation	Design	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/22/26	09/02/26	
1	Deerfield Run ES	FY/22	County Funded	\$505,002	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	03/04/24	08/30/24	98%
7	District Heights ES	FY/15	County Funded	\$400,000	Kitchen & Food Services	Replace Exhaust System & Walk-in Refrigerator and Add Walk-in Freezer and Combination Oven.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/27/18	09/01/18	100%
7	District Heights ES	FY/16	County Funded	\$36,735	Abatement	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/09/16	100%
7	District Heights ES	FY/16	County Funded	\$125,000	Kitchen & Food Services	Kitchen Renovation - This project includes the disconnection, removal, and disposal of the dishwasher, dishwasher hood, dishwasher tables, booster heater and create opening in wall to allow access to new walk-in freezer.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	09/20/17	10/31/17	100%
7	District Heights ES	FY/17	State & County Funded	\$255,000	Systemic Upgrades: HVAC	Roof Top Units (RTUs) Replacement: includes replacing 2 existing roof mount units with high efficiency HVAC units with variable speed frequency drives.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	05/01/17	07/10/17	100%
7	District Heights ES	FY/18	County Funded	\$2,442,999	Building Repairs: Major/Emergency	Limited Renovations (Interior Architectural) Phase I	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	04/08/19	09/03/19	100%
7	District Heights ES	FY/18	County Funded	\$1,819,369	Building Repairs: Major/Emergency	Modular Classrooms & Asbestos Remediation Phase II	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	03/18/19	09/03/19	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
7	District Heights ES	FY/19	County Funded	\$2,991,451	Systemic Upgrades: HVAC	AC Upgrades Phase I	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	04/08/19	09/03/19	100%
7	District Heights ES	FY/22	County Funded	\$27,000	Kitchen & Food Services	Serving Line Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	08/08/23	08/12/23	100%
2	Dora Kennedy French Immersion	FY/26	TBD (currently tracking for other programs)		Other	Facility Move/Closure – Summer 2026 This entry is to track facilities that will be unavailable during Summer 2026 activities due to a scheduled move or closure.	Planning	<a href="mailto:kalisa.bell@pgcps.org">kalisa.bell@pgcps.org</a>			
7	Drew Freeman MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/10/16	100%
7	Drew Freeman MS	FY/16	State & County Funded	\$2,783,000	Systemic Upgrades: HVAC	Unit Ventilator, Exhaust Fans & AHUs Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
7	Drew Freeman MS	FY/16	State & County Funded	\$5,977,000	Systemic Upgrades: Electrical	Lighting and Wiring Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
7	Drew Freeman MS	FY/26	TBD (currently tracking for other programs)		Other	Major Maintenance Repairs for P3 Schools – Summer 2026 This entry is to track facilities that will be unavailable during Summer 2026 activities due to scheduled maintenance and repairs.	Planning				
1	DuVal HS	FY/14	County Funded	\$821,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academies of Consumer Sciences, Hospitality: Tourism, Engineering & Science and Graphics, Arts, Media and Communications (Priority 63).	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	06/15/17	08/22/17	98%
1	DuVal HS	FY/17	State & County Funded	\$2,556,000	Exterior Door/Window Upgrades	Window Replacement: total of 655 windows to be replaced. Include demolishing existing window system, removal of all related debris and the installation of heavy commercial grade single hung aluminum windows with double insulated units.	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	06/19/19	08/02/21	98%
1	DuVal HS	FY/22	County Funded	\$1,500,000	Systemic Upgrades: HVAC	Main Bldg. - 2 RTUs, Fan Coil, Controls Annex - Cafeteria RTU, 5 RTU	Substantially Complete	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/27/22	09/30/24	98%
1	DuVal HS	FY/24	County Funded	\$82,761	ADA Upgrades	Lift Replacement (Stage)	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	11/01/24	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	DuVal HS	FY/24	Operating Funds	\$300,000	Abatement	Asbestos Abatement	In Construction	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24	08/11/24	100%
1	DuVal HS	FY/25	State-ASP Funded	\$1,209,426	Athletic Improvements	Football Stadium Bleachers & Press-box Replacement.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/22/26	09/02/26	
1	Dwight Eisenhower MS	FY/17	State & County Funded	\$384,000	Exterior Door/Window Upgrades	Storefront Replacement: includes demo, abatement and replacement of existing exterior storefront doors and windows with new aluminum system.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	08/13/18	02/22/19	100%
1	Dwight Eisenhower MS	FY/19	State & County Funded	\$12,063,600	Systemic Upgrades: HVAC	HVAC & Building Envelope / Replace the 1969-1974 central controls system, HVAC piping, all ten (10) AHUs, 45 finned tube radiators, four (4) self-contained unit ventilators, 17 floor mounted fan coil units, two (2) ceiling mounted AHUs, chiller	Contractor Procurement	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>	06/07/21	08/18/25	48%
1	Dwight Eisenhower MS	FY/20	County Funded	\$296,584	Security Upgrades	Provide and install the following: 1. (132) One Hundred Thirty-two IP Network Cameras (45- Outside, 87- Inside) 2. 170TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/10/20	07/31/20	100%
1	Dwight Eisenhower MS	FY/26	County Funded	\$21,435	Building Repairs: Minor	Dance Studio Flooring Replacement	In Construction	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
2	Eleanor Roosevelt HS	FY/15	State & County Funded	\$903,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 1 Pod-(6 classrooms). Project required to remove the temporary partitions and replace them with permanent partitions.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/15/18	09/02/18	100%
2	Eleanor Roosevelt HS	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/17	03/30/19	0%
2	Eleanor Roosevelt HS	FY/15	County Funded	\$102,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements	Substantially Complete	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/23/15	08/19/15	99%
4	Ellen Ochoa MS (former New Glenridge Area MS)	FY/20	State & County Funded	\$80,145,734	New Schools & Modernizations	New Middle School to be built in the Glenridge area	In Construction	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	12/27/21	05/01/24	99%
6	Ernest Everett Just MS	FY/20	County Funded	\$274,108	Security Upgrades	Provide and install the following: 1. (119) One Hundred Nineteen IP Network Cameras (40- Outside, 79- Inside) 2. 170TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	06/29/20	10/31/20	100%
6	Ernest Everett Just MS	FY/26	County Funded	\$1,000,000	Systemic Upgrades: HVAC	Controls Replacement	Scope Development	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/22/26	08/14/26	
9	Eugene Burroughs MS / Accokeek Academy	FY/19	County Funded	\$12,546	Security Upgrades	Install card access on three door 6,7 and 8	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	07/13/20	12/04/20	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Eugene Burroughs MS / Accokeek Academy	FY/20	County Funded	\$94,518	Security Upgrades	Upgrade camera system head end equipment to Genetec.	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	02/14/20	06/30/20	100%
9	Facilities Administration Building	FY/21	County Funded	\$8,000,000	Building Repairs: Major/Emergency	HVAC and Architectural Finishes	In Construction	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	09/07/22	09/01/23	99%
9	Facilities Administration Building	FY/21	County Funded	\$61,042	Abatement	Asbestos Abatement	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	12/16/19	01/03/20	100%
9	Facilities Service Base	FY/24	County Funded	\$109,280	Systemic Upgrades: Electrical	Generator Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_keelan.hendricks@pgcps.org">pg_keelan.hendricks@pgcps.org</a>	12/20/24		100%
4	Fairmont Heights HS (Replacement)	FY/12	State & County Funded	\$79,912,000	New Schools & Modernizations	Facility Replacement - This project will deliver a state-of-the-art new facility designed for a State Rated Capacity of 953 students on a 38.7-acre site with an overall sq. ft. of 190,058.	Substantially Complete	<a href="mailto:nadine.belizaire@pgcps.org">nadine.belizaire@pgcps.org</a>	09/15/15	12/31/21	97%
4	Fairmont Heights HS (Replacement)	FY/16	State & County Funded	\$14,665,000	New Schools & Modernizations	Facility Replacement - This project will deliver a state-of-the-art new facility designed for a State Rated Capacity of 953 students on a 38.7-acre site with an overall sq. ft. of 190,058.	Substantially Complete	<a href="mailto:nadine.belizaire@pgcps.org">nadine.belizaire@pgcps.org</a>	09/15/15	12/31/21	97%
4	Fairmont Heights HS (Replacement)	FY/20	County Funded	\$563,536	Athletic Improvements	Scoreboard Installation for Football, Baseball and Softball Fields	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	07/24/23	11/20/24	100%
8	Flintstone ES	FY/17	State & County Funded	\$1,213,000	Systemic Upgrades: HVAC	Piping Replacement: includes removal and replacement of all existing steam supply and return piping, steam traps, satellite condensate tanks, pipe supports on the dual pipe distribution system.	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	06/01/19	08/15/19	95%
8	Flintstone ES	FY/24	County Funded	\$175,000	Parking Lots	Parking Lot Refurbishment	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	08/09/24	100%
8	Flintstone ES	FY/25	County Funded	\$817,496	Building Repairs: Major/Emergency	Exterior Wall Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
8	Forest Heights ES	FY/15	County Funded	\$45,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/23/15	08/19/15	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Forest Heights ES	FY/18	County-Rosecroft Funded	\$34,211	IT Upgrades	Electronic Sign (FY18 Rosecroft Funds \$9,210.52; FY20 Rosecroft Funds \$25,000)	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	02/15/21	06/20/21	100%
8	Forest Heights ES	FY/24	State-HSFF Funded	\$1,859,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	03/28/25	10/29/25	100%
7	Forestville HS	FY/16	State & County Funded	\$753,000	Systemic Upgrades: Misc	Final Phase Roof Replacement - The scope of this project will be to remove and replace approximately 21,600 sf of the 1965 section of this building and approximately 1,200 of the 1993 additions to the 1965 building.	Substantially Complete	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	06/15/18	10/30/18	98%
7	Forestville HS	FY/26	Operating Funds	\$1,434,701	Systemic Upgrades: HVAC	Controls Upgrade	In Construction	<a href="mailto:jason.walker@pgcps.org">jason.walker@pgcps.org</a>			
8	Fort Foote ES	FY/18	County-Rosecroft Funded	\$34,211	IT Upgrades	Electronic Sign (FY18 Rosecroft Funds \$9,210.52; FY20 Rosecroft Funds \$25,000)	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	02/15/21	06/20/21	100%
8	Fort Foote ES	FY/21	County Funded	\$93,243	Security Upgrades	Install, program and test Forty IP Network Cameras (18- Outside, 22- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	05/17/21	06/30/21	
8	Fort Foote ES	FY/26	State-HSFF Funded	\$1,792,174	Systemic Upgrades: Misc	Replacement of approximately 49,000 sf of roof installed in 2004. This is a full roof replacement.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
8	Fort Foote ES	FY/26	County Funded	\$500,000	Playgrounds	Playground Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
9	Fort Washington Forest ES	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%
1	Frances Fuchs ECC	FY/26	County Funded	\$200,000	Code Corrections	Fire Alarm System Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
6	Francis Scott Key ES	FY/19	County Funded	\$129,769	Security Upgrades	Provide and install the following: 1. (51) Forty-nine IP Network Cameras (18- Outside, 33- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	09/01/19		100%
9	Francis T. Evans ES	FY/15	State & County Funded	\$3,234,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 3 Pods	Substantially Complete	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	06/15/18	09/30/18	98%
9	Francis T. Evans ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	09/19/16	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
9	Francis T. Evans ES	FY/26	County Funded	\$640,689	Playgrounds	Playground Replacement (PreK, K-6)	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
9	Frederick Douglass HS	FY/22	County Funded	\$9,000,000	Athletic Improvements	Football Stadium Renovation	In Construction	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	05/12/25	08/31/26	75%
9	Frederick Douglass HS	FY/25	County Funded	\$64,200	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	10/06/25	10/10/25	100%
8	Friendly HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/10/16	100%
8	Friendly HS	FY/23	County Funded	\$237,760	Building Repairs: Minor	Tennis Court Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/19/23	08/18/23	100%
8	Friendly HS	FY/23	County Funded	\$604,450	Building Repairs: Minor	Running Track Upgrade	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/19/23	08/18/23	100%
8	Friendly HS	FY/24	County Funded	\$47,044	Building Repairs: Minor	Corridor and Locker Room Locker Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_keelan.hendricks@pgcps.org">pg_keelan.hendricks@pgcps.org</a>	06/15/24	06/24/24	100%
6	G. James Gholson MS	FY/21	County Funded	\$400,000	Security Upgrades	New IP camera system	Design	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
4	Gaywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/10/16	100%
4	Gaywood ES	FY/17	State & County Funded	\$831,000	Systemic Upgrades: HVAC	Univent Replacement: includes replacing 29, 1958 classroom steam heat unit ventilators with 8 radiator and 8 fan coil units.	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	06/21/18	08/20/18	99%
4	Gaywood ES	FY/18	County Funded	\$350,000	Kitchen & Food Services	Remove roll-down door and close opening. Remove dishwasher hood. Add combination walk-in refrigerator & freezer.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/15/19	08/28/19	99%
4	Gaywood ES	FY/24	County Funded	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		20%
4	Glenn Dale ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/12/16	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Glenridge ES	FY/26	TBD (currently tracking for other programs)		Other	Facility Move/Closure – Summer 2026 This entry is to track facilities that will be unavailable during Summer 2026 activities due to a scheduled move or closure.	Planning	<a href="mailto:kalisa.bell@pgcps.org">kalisa.bell@pgcps.org</a>			
2	Greenbelt ES	FY/17	State & County Funded	\$1,214,000	Systemic Upgrades: HVAC	Chiller Replacement & HVAC Controls Upgrade: includes removing two 1993, 120 ton air cooled Trane chillers.	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/25/18	08/24/18	100%
2	Greenbelt ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (58) Fifty-eight IP Network Cameras (24- Outside, 35- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/03/20	04/30/20	100%
2	Greenbelt ES	FY/22	State-HSFF Funded	\$3,360,665	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/24/24	09/04/24	100%
2	Greenbelt MS Bus lot (old)	FY/19	County Funded		Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Greenbelt Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	Design	<a href="mailto:cfloek@pgcps.org">cfloek@pgcps.org</a>			0%
9	Gwynn Park HS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/10/16	100%
9	Gwynn Park HS	FY/25	County Funded	\$48,150	Building Repairs: Minor	Gym Fan Installation	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	10/17/25	11/14/25	100%
9	Gwynn Park HS	FY/26	TBD (currently tracking for other programs)		Athletic Improvements	Turf Replacement (This project has been entered into QB for tracking under the 2026 Facilities Improvement Summer Program. Limited details are currently available. Please contact the assigned PM for additional information.)	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
6	H. Winship Wheatley ECC	FY/23	State & County Funded		Systemic Upgrades: HVAC	HVAC Replacement	Design	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>			
7	Henry Wise Jr. HS	FY/19	County Funded	\$25,000	Kitchen & Food Services	Remove and Replace (1) New Serving Line	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	11/15/23	02/26/21	100%
7	Henry Wise Jr. HS	FY/26	TBD (currently tracking for other programs)		Athletic Improvements	Turf Replacement (This project has been entered into QB for tracking under the 2026 Facilities Improvement Summer Program. Limited details are currently available. Please contact the assigned PM for additional information.)	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
5	High Bridge ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	03/30/19	0%
5	High Bridge ES	FY/24	County Funded	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
1	High Point HS	FY/19	County Funded	\$50,000	Kitchen & Food Services	Remove and Replace (2) New Serving Lines	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	10/01/20	02/26/21	100%
1	High Point HS	FY/19	County Funded	\$231,584	Building Repairs: Minor	Structural Project	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	11/24/20	01/29/21	100%
1	High Point HS	FY/24	County Funded	\$450,000	ADA Upgrades	Elevator Modernization	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	09/12/24	100%
1	High Point HS	FY/24	State-Design Services	\$8,570,000	New Schools & Modernizations	Replacement of the existing 318,376 SF,2081-seat high school with a new 423,000 SF high school on the same site with a capacity of 2600 students.	Planning	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>			
6	Highland Park ES	FY/17	State & County Funded	\$1,724,000	Systemic Upgrades: HVAC	Piping, Insulation & Boiler Replacement: includes removing the two 1994 hot water boilers, installing two new energy efficient boilers, system pumps and expansion tank. Included is the installation of a limited sprinkler system in that area.	Substantially Complete	<a href="mailto:nadine.belizaire@pgcps.org">nadine.belizaire@pgcps.org</a>	06/28/19	10/25/19	98%
6	Highland Park ES	FY/20	County Funded	\$173,326	Security Upgrades	Provide and install the following: 1. (73) Forty-nine IP Network Cameras (28- Outside, 45- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	07/27/20	08/31/20	100%
6	Highland Park ES	FY/20	County Funded	\$333,167	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	02/28/24	08/30/24	98%
6	Highland Park ES	FY/25	County Funded	\$43,228	Playgrounds	Playground Refurbishment	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/09/25	06/13/25	100%
8	Hillcrest Heights ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements. Financial close-out in progress	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/17/16	100%
8	Hillcrest Heights ES	FY/24	County Funded	\$600,000	Systemic Upgrades: HVAC	Two (2) Boiler Replacements	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/24/24	10/14/24	98%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
8	Hillcrest Heights ES	FY/25	State-HSFF Funded	\$2,727,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	03/28/25	11/12/25	100%
2	Hollywood ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/10/16	100%
2	Hollywood ES	FY/17	State & County Funded	\$766,000	Systemic Upgrades: HVAC	Boiler Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/20/20	08/24/20	100%
2	Hollywood ES	FY/24	Operating Funds	\$150,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
1	Howard B. Owens Science Center	FY/23	County Funded	\$2,000,000	Building Repairs: Minor	Minor Renovation - Interior and Exterior	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	04/24/23	08/16/24	100%
1	Howard B. Owens Science Center	FY/24	County Funded	\$190,800	Other	Marquee Sign Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	07/12/24	100%
3	Hyattsville ES	FY/15	County Funded	\$62,477	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project used to be in compliance.	Substantially Complete	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/24/19	08/14/19	99%
3	Hyattsville ES	FY/16	State & County Funded	\$3,472,000	Systemic Upgrades: HVAC	Fan Coil Units & AHUs Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	08/31/18	95%
3	Hyattsville ES	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovation	In Construction	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>			
3	Hyattsville MS	FY/26	TBD (currently tracking for other programs)		Other	Major Maintenance Repairs for P3 Schools – Summer 2026  This entry is to track facilities that will be unavailable during Summer 2026 activities due to scheduled maintenance and repairs.	Planning				
8	Indian Queen ES	FY/15	State & County Funded	\$4,389,000	Renovations: Pod Conversions	Phase I - Open Space Pod Conversion Renovations / 4 Pods	Substantially Complete	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	12/20/16	04/25/18	98%
1	James E. Duckworth SC	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	09/30/19	0%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
1	James H. Harrison ES	FY/20	County Funded	\$148,662	Security Upgrades	Provide and install the following: 1. (57) Fifty-seven IP Network Cameras (23- Outside, 34- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43-inch Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	12/12/19	01/31/20	100%
9	James Madison MS	FY/20	State & County Funded	\$10,421,000	Systemic Upgrades: HVAC	Replacement of HVAC piping system, chiller, cooling tower, four (4) air handling units, 96 mixing boxes, twenty (20) finned tube radiators, fifteen (15) convectors, and controls.	Substantially Complete	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>	06/24/22		98%
9	James Madison MS	FY/25	Grant Funded-ESSER	\$3,229,269	Renovations: Misc	Modular Addition	Contractor Procurement	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	08/01/23	07/31/24	98%
9	James Madison MS	FY/25	State-HSFF Funded	\$3,450,680	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	04/16/25	10/24/25	100%
4	James McHenry ES	FY/25	Operating Funds		Kitchen & Food Services	Construction and installation exterior of walk-in freezer with interior kitchen entry	In Construction	<a href="mailto:clay.berry@pgcps.org">clay.berry@pgcps.org</a>	06/19/25	08/15/25	0%
4	James McHenry ES	FY/26	County Funded	\$209,000	Code Corrections	Fire Alarm System Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
8	James Ryder Randall ES	FY/23	County Funded	\$244,500	Code Corrections	Fire Alarm Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	11/01/24	100%
8	James Ryder Randall ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
8	John Hanson Montessori	FY/23	County Funded	\$315,888	Building Repairs: Major/Emergency	Corridor and Locker Room Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_keelan.hendricks@pgcps.org">pg_keelan.hendricks@pgcps.org</a>	06/30/22	11/30/22	100%
8	John Hanson Montessori	FY/26	TBD (currently tracking for other programs)		Other	Facility Move/Closure – Summer 2026  This entry is to track facilities that will be unavailable during Summer 2026 activities due to a scheduled move or closure.	Planning	<a href="mailto:kalisa.bell@pgcps.org">kalisa.bell@pgcps.org</a>			
4	Judge Sylvania Woods ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	02/10/17	100%
4	Judge Sylvania Woods ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/22/20	08/21/20	95%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Judge Sylvania Woods ES	FY/21	County Funded	\$137,075	Security Upgrades	Install, program and test Sixty-five IP Network Cameras (25- Outside, 40- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	05/03/21	06/30/21	100%
4	Kenmoor ECC	FY/24	County Funded	\$377,969	Exterior Door/Window Upgrades	Exterior Doors and Storefront Windows Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	07/22/24	02/21/25	100%
4	Kenmoor MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	09/05/16	01/30/17	100%
4	Kenmoor MS	FY/19	County Funded	\$199,681	Security Upgrades	Provide and install the following: 1. (90) Ninety IP Network Cameras (23- Outside, 67- Inside) 2. 130TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC with a 22" Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	04/29/19	07/26/19	100%
4	Kenmoor MS	FY/24	Operating Funds	\$250,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
4	Kenmoor MS	FY/26	TBD (currently tracking for other programs)		Other	Facility Move/Closure – Summer 2026 This entry is to track facilities that will be unavailable during Summer 2026 activities due to a scheduled move or closure.	Planning	<a href="mailto:kalisa.bell@pgcps.org">kalisa.bell@pgcps.org</a>			
4	Kenmoor MS	FY/26	TBD (currently tracking for other programs)		Other	Major Maintenance Repairs for P3 Schools – Summer 2026 This entry is to track facilities that will be unavailable during Summer 2026 activities due to scheduled maintenance and repairs.	Planning				
6	Kettering ES	FY/20	County Funded	\$386,182	Systemic Upgrades: HVAC	Chiller Replacement	In Construction	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	02/28/24	08/30/24	97%
6	Kettering MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	01/31/17	100%
6	Kettering MS	FY/19	County Funded	\$276,430	Building Repairs: Major/Emergency	Modular Roof Replacement	Substantially Complete	<a href="mailto:Lance.Schiemer@pgcps.org">Lance.Schiemer@pgcps.org</a>	06/30/21	08/30/21	100%
6	Kettering MS	FY/22	County Funded	\$2,604,262	Renovations: Misc	Provide (10) classroom modular additions	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	08/01/22	08/07/23	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Kettering MS	FY/23	Grant Funded (see description)	\$2,000,000	Systemic Upgrades: HVAC	HVAC Upgrades	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	07/03/24	09/30/24	100%
5	Kingsford ES	FY/15	County Funded	\$300,000	Parking Lots	Major Repairs Driveways, Parking Lots & Entrance Project	Design	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/18	03/30/19	0%
5	Kingsford ES	FY/18	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Chiller Replacement	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/22/20	08/21/20	95%
5	Kingsford ES	FY/26	County Funded	\$200,000	Building Repairs: Minor	Operable Wall Replacement	Scope Development	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
6	Lake Arbor ES	FY/19	County Funded	\$137,681	Security Upgrades	Provide and install the following: 1. (60) Sixty IP Network Cameras (17- Outside, 43- Inside) 2. 100TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC with a	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	04/01/19	06/01/19	100%
2	Lamont ES	FY/19	County Funded	\$9,283,427	Systemic Upgrades: HVAC	HVAC / Replace the 1964/1966 HVAC system, domestic water piping, plumbing fixtures, 31 windows, 29 exterior doors, ceilings, lighting, and fire alarm system, and install a sprinkler system.	Design	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/27/25	06/12/26	0%
2	Lamont ES	FY/19	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/27/22	08/26/22	100%
6	Largo HS	FY/14	State & County Funded	\$981,125	Systemic Upgrades: HVAC	Air Conditioning Initiative (ACI) - Provide air conditioning in the 1970 school building gymnasium by installing a rooftop packaged air conditioning units and all associated interior duct work.	Substantially Complete	<a href="mailto:kmuse@pgcps.org">kmuse@pgcps.org</a>	06/14/17	10/13/17	98%
6	Largo HS	FY/15	State & County Funded	\$964,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Business and Finance	Substantially Complete	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	12/28/16	10/01/19	99%
6	Largo HS	FY/15	State & County Funded	\$4,261,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 5 Pods-Phase I	Substantially Complete	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	12/28/16	08/12/18	99%
6	Largo HS	FY/16	State & County Funded	\$3,586,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academy of Health & Biosciences.	Substantially Complete	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	06/15/17	08/19/20	99%
1	Laurel Bus Lot	FY/15	County Funded	\$285,700	Central Garage & Transportation	Laurel Bus Lot Project - A revised Capital Plan needs to be developed with the Department of Transportation and Central Garage.	Planning	<a href="mailto:cfloek@pgcps.org">cfloek@pgcps.org</a>			0%
1	Laurel HS	FY/20	Grant Funded (see description)	\$6,500,000	Athletic Improvements	Football Stadium Renovation	Design	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>		02/16/24	

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Lewisdale ES	FY/16	State & County Funded	\$289,000	Systemic Upgrades: HVAC	RTU Replacement - The scope of this project will be to remove and replace 7 Roof Top Units (RTUs) in the 1953 building. The new units will have digital control and tie-in to our EMS.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/01/19	08/30/19	100%
7	Longfields ES	FY/22	County Funded	\$500,000	Renovations: Misc	Staged Renovation	Planning	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/14/24		0%
2	Magnolia ES	FY/23	County Funded	\$205,000	Parking Lots	Parking Lot & Existing Areas	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/19/23	08/11/23	100%
2	Magnolia ES	FY/24	County Funded	\$210,000	Code Corrections	Fire Alarm System Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/30/25	11/05/25	100%
2	Margaret Brent SC	FY/21	County Funded	\$2,000,000	New Schools & Modernizations	Renovation/Replacement	Planning	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>			
9	Marlton ES	FY/17	State & County Funded	\$875,000	Systemic Upgrades: HVAC	Piping Insulation Replacement & Controls Upgrade: includes total replacement of the existing pneumatic controls. Also includes the replacement of valves, dampers, sensors, actuators, and safety controls.	Substantially Complete	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/25/18	08/24/18	98%
1	Martin Luther King Jr. MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirement	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/15/16	100%
1	Martin Luther King Jr. MS	FY/23	County Funded	\$70,000	Building Repairs: Minor	Dance Floor Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_keelan.hendricks@pgcps.org">pg_keelan.hendricks@pgcps.org</a>	07/20/23	08/18/23	100%
1	Martin Luther King Jr. MS	FY/26	State & County Funded	\$3,428,811	Systemic Upgrades: Misc	Replace the 1972 89,899 sf built-up roof.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
3	Mary Harris Jones ES	FY/19	County Funded	\$140,895	Security Upgrades	Provide and install the following: 1. (61) Sixty One IP Network Cameras (17- Outside, 44- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	08/08/19	04/01/20	100%
6	Maya Angelou French Immersion	FY/22	County Funded	\$132,416	ADA Upgrades	Lift Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	09/16/24	10/18/24	100%
6	Maya Angelou French Immersion	FY/26	County Funded	\$200,000	Parking Lots	Parking Lot Refurbishment	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
5	Meadowbrook ES	FY/24	County Funded	\$116,510	ADA Upgrades	Lift Installation - Structural Alterations in Stairwell	In Construction	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	90%
9	Melwood ES	FY/15	State & County Funded	\$1,661,000	Renovations: Pod Conversions	Open Space Pod Conversion Renovations / 2 Pods	Substantially Complete	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/15/17	08/18/17	95%
9	Melwood ES	FY/17	State & County Funded	\$575,000	Exterior Door/Window Upgrades	Storefront & Window Wall Replacement: A total of 19 windows and 1 double door will be replaced. Includes demolishing existing storefront system and remove all related debris, install new aluminum storefront system and entrance doors.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	08/20/18	02/22/19	100%
9	Melwood ES	FY/19	County Funded	\$1,700,000	Parking Lots	Parking Lot Improvements	Design	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>	02/02/24	08/14/26	0%
9	Melwood ES	FY/20	County Funded	\$109,738	Security Upgrades	Provide and install the following: 1. (42) Forty-nine IP Network Cameras (17- Outside, 25- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	12/02/19	02/28/20	100%
9	Melwood ES	FY/26	State & County Funded	\$3,550,000	Systemic Upgrades: Misc	Replace the 1996 65,985 sf built-up roof.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
9	Melwood ES	FY/26	County Funded	\$200,200	Code Corrections	Fire Alarm System Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
5	Mullikin Bus Lot	FY/19	County Funded	\$250,000	Central Garage & Transportation	Construction of Administrative Office and Bus Depot at Mullikin Transportation Facility; Prepare Concept Design for Laurel and Douglass Transportation Facilities	In Construction	<a href="mailto:don.howerton@pgcps.org">don.howerton@pgcps.org</a>	04/01/24	11/15/24	30%
3	New Northern Adelphi Area HS	FY/26	State-Design Services	\$10,168,000	New Schools & Modernizations	Construction of a new 369,806 SF and 2,600 student high school in the Adelphi area to alleviate current overcrowding in neighboring schools and meet the demands of projected enrollment.	Design	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>			0%
3	Nicholas Orem MS	FY/14	State & County Funded	\$1,000,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	<a href="mailto:kmuse@pgcps.org">kmuse@pgcps.org</a>	06/14/17	10/30/17	99%
3	Nicholas Orem MS	FY/22	County Funded	\$800,000	Kitchen & Food Services	Kitchen Renovation	Substantially Complete	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/24/25	10/02/25	99%
3	Nicholas Orem MS	FY/26	County Funded	\$400,000	Building Repairs: Minor	Multipurpose Room Stage Refurbishment	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
7	North Forestville ES	FY/14	State & County Funded	\$800,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	<a href="mailto:kmuse@pgcps.org">kmuse@pgcps.org</a>	06/14/17	09/29/17	99%
7	North Forestville ES	FY/17	State & County Funded	\$639,000	Systemic Upgrades: HVAC	Boiler Replacement: includes removal of two 60 hp steam boilers and 1/4 hp return pumps and replacing them with two new energy efficient 60 hp boilers, boiler feed system and return pumps.	Substantially Complete	<a href="mailto:nadine.belizaire@pgcps.org">nadine.belizaire@pgcps.org</a>	10/05/18	12/28/18	99%
5	Northview ES	FY/21	County Funded	\$200,000	Security Upgrades	New IP Camera system	Scope Development	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
3	Northwestern HS	FY/15	County Funded	\$797,000	Renovations: Career Academy	Secondary School Reform (SSR) - Renovations for the academic academies of Business & Finance	Contractor Procurement	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	06/23/20		0%
3	Northwestern HS	FY/16	County Funded	\$98,000	Renovations: Career Academy	Secondary School Reform (SSR) - This renovation will be for the Academy for Performing Arts.	Contractor Procurement	<a href="mailto:hiwot.haileselassie@pgcps.org">hiwot.haileselassie@pgcps.org</a>	06/23/20	08/15/20	0%
3	Northwestern HS	FY/21	County Funded	\$497,321	Security Upgrades	Install program and test Two hundred Forty-five IP Network Cameras (46- Outside, 195- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	In Construction	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/08/21	06/30/21	
8	Oxon Hill ES	FY/23	Operating Funds	\$1,000,000	Systemic Upgrades: HVAC	Chiller and Cooling Tower Replacement	Substantially Complete	<a href="mailto:garth.deitzer@pgcps.org">garth.deitzer@pgcps.org</a>	07/03/23		80%
8	Oxon Hill ES	FY/23	County Funded	\$28,000	Parking Lots	Play Court Refurbishment	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/19/23	08/11/23	100%
8	Oxon Hill ES	FY/24	County Funded	\$210,000	Code Corrections	Fire Alarm System Replacement	In Construction	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/30/25		99%
8	Oxon Hill HS	FY/18	County Funded	\$231,489	Security Upgrades	Provide and install the following: 1. (118) One Hundred-Eighteen IP Network Cameras (24-Outside, 94- Inside) 2. 154TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-M	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	07/01/18	11/15/18	100%
8	Oxon Hill HS	FY/24	County Funded	\$600,000	Athletic Improvements	Running Track Refurbishment	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
8	Oxon Hill HS	FY/26	County Funded	\$637,900	Building Repairs: Minor	Gym Bleacher Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
8	Oxon Hill HS	FY/26	TBD (currently tracking for other programs)		Athletic Improvements	Turf Replacement (This project has been entered into QB for tracking under the 2026 Facilities Improvement Summer Program. Limited details are currently available. Please contact the assigned PM for additional information.)	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
8	Oxon Hill MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	08/17/16	100%
8	Oxon Hill MS	FY/16	State & County Funded	\$6,184,000	Systemic Upgrades: HVAC	Fan Coil Units Replacement - The scope of this project will include the replacement of 33 Univents and 11 Convection Heat Units in the 1972 building. The scope will also include new supply and return piping.	Substantially Complete	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	12/01/17		99%
8	Oxon Hill MS	FY/24	State-HSFF Funded	\$2,500,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/24/24	09/10/24	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Paint Branch ES	FY/22	County Funded	\$257,444	Building Repairs: Major/Emergency	Interior Doors Replacement	Substantially Complete	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	09/09/24	12/27/24	100%
2	Paint Branch ES	FY/23	Operating Funds		Building Repairs: Minor	Flooring Replacement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	07/03/23		
2	Paint Branch ES	FY/24	County Funded	\$210,000	Code Corrections	Fire Alarm System Replacement	In Construction	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	01/05/26	08/14/26	30%
2	Paint Branch ES	FY/24	Operating Funds	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
2	Parkdale HS	FY/23	County Funded	\$500,000	Parking Lots	Parking Lot - Existing Areas	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/19/23	08/11/23	100%
2	Parkdale HS	FY/23	Operating Funds		Abatement	Asbestos Removal	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	07/03/23		
2	Parkdale HS	FY/23	Operating Funds		Building Repairs: Minor	Flooring Replacement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	07/03/23		
2	Parkdale HS	FY/25	County Funded	\$51,360	Building Repairs: Minor	Gym Fan Installation	In Construction	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	10/17/25	10/31/25	90%
2	Parkdale HS	FY/26	County Funded	\$736,000	ADA Upgrades	Two Elevator Modernizations (PG3086 and PG3468)	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
2	Parkdale HS	FY/26	County Funded	\$900,000	Systemic Upgrades: HVAC	Two (2) air cooled chillers, condenser piping, and boiler room piping replacement.	Scope Development	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	06/22/26	08/14/26	
5	Patuxent ES	FY/20	State & County Funded	\$5,866,000	Systemic Upgrades: HVAC	Replace HVAC System to include the existing hydronic piping system, air cooled chiller, two (2) air handlers, one (1) 15 ton condensing unit, twenty-two (22) fan coil units.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/01/22	05/17/23	100%
5	Patuxent ES	FY/20	County Funded	\$157,099	Security Upgrades	Provide and install the following: 1. (61) Sixty-one IP Network Cameras (27- Outside, 34- Inside) 2. 120TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	01/30/20	06/01/20	100%
6	Phyllis E. Williams ES	FY/19	County Funded	\$122,034	Security Upgrades	Provide and install the following: 1. (50) Fifty IP Network Cameras (19- Outside, 31- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/04/19	05/31/19	100%
6	Phyllis E. Williams ES	FY/23	State & County Funded	\$3,120,000	Systemic Upgrades: HVAC	Piping / Replace 1976 HVAC equipment, including 16 hydronic cabinet unit heaters, 48 VAV terminal boxes, the hydronic piping system and distribution pumps, and replace ceilings and lighting fixtures.	In Construction	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	10/02/23	06/30/24	45%

**Prince George's County Public Schools**  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
**January 2026**

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Phyllis E. Williams ES	FY/26	TBD (currently tracking for other programs)		Systemic Upgrades: HVAC	Switchgear Replacement (This project has been entered into QB for tracking under the 2026 Facilities Improvement Summer Program. Limited details are currently available. Please contact the assigned PM for additional information.)	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
5	Pointer Ridge ES	FY/22	County Funded	\$27,515	Building Repairs: Major/Emergency	Bathroom Partition Replacement	Substantially Complete	<a href="mailto:Lance.Schiemer@pgcps.org">Lance.Schiemer@pgcps.org</a>	06/30/22	08/12/22	100%
5	Pointer Ridge ES	FY/24	County Funded	\$200,000	Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
4	Port Towns ES	FY/20	County Funded	\$148,511	Security Upgrades	Provide and install the following: 1. (66) Forty-nine IP Network Cameras (22- Outside, 44- Inside) 2. 90TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	02/03/20	06/30/20	100%
8	Potomac HS	FY/15	State & County Funded	\$3,492,000	Renovations: Career Academy	Secondary School Reform Renovations for the academic academies of Law Education & Public Service, Environmental Science with Greenhouse Addition	Contractor Procurement	<a href="mailto:cfloeck@pgcps.org">cfloeck@pgcps.org</a>	06/12/24	09/18/24	
8	Potomac HS	FY/22	County Funded	\$500,000	Renovations: Misc	Auxiliary Gym Roof Replacement	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	05/15/24	06/28/24	100%
9	Potomac Landing ES	FY/26	TBD (currently tracking for other programs)		Renovations: Classroom	Modular Addition	Planning	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>		08/03/26	3%
7	Princeton ES	FY/14	State & County Funded	\$500,000	Systemic Upgrades: HVAC	Condensate Piping Infrastructure Replacement	Substantially Complete	<a href="mailto:kmuse@pgcps.org">kmuse@pgcps.org</a>	06/14/17	09/29/17	98%
7	Princeton ES	FY/17	State & County Funded	\$1,278,000	Systemic Upgrades: HVAC	Steam Trap Vent Lines & Univent Replacement: work is to replace the leaking condensate piping and steam trap leaks. The scope also includes asbestos abatement.	Final Completion (Closeout Approval Requested)	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	06/21/18	08/20/18	99%
7	Princeton ES	FY/24	State-HSFF Funded	\$2,110,000	Systemic Upgrades: Misc	Roof Replacement (HSFF)	Substantially Complete	<a href="mailto:diego.gonzalezguzman@pgcps.org">diego.gonzalezguzman@pgcps.org</a>	06/24/25	09/30/25	100%
3	Ridgecrest ES	FY/21	County Funded	\$17,149	Building Repairs: Minor	Water Main Replacement	In Construction	<a href="mailto:edward.roebuck@pgcps.org">edward.roebuck@pgcps.org</a>	06/30/21	08/04/21	
3	Ridgecrest ES	FY/24	County Funded	\$75,000	Systemic Upgrades: Misc	Replacement of emergency escape windows in all classrooms	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/17/24	10/12/24	100%
2	Riverdale ES	FY/18	State & County Funded	\$305,429	Systemic Upgrades: HVAC	Replace one (1) rooftop unit serving the kitchen, one (1) air handling unit serving the north and south perimeter, and one (1) exhaust fan serving the boiler room, installed in 1978, and integrate with energy management system.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/27/22	08/29/22	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
2	Riverdale ES	FY/20	County Funded	\$500,000	Kitchen & Food Services	Kitchen Renovation: Remove existing kitchen equipment and replace/upgrade with new.	Substantially Complete	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/27/22	08/26/22	99%
2	Riverdale ES	FY/26	County Funded	\$136,752	Systemic Upgrades: HVAC	Cooling Tower	Contractor Procurement	<a href="mailto:pg_sean.mccoy@pgcps.org">pg_sean.mccoy@pgcps.org</a>	04/22/26	08/14/26	
2	Robert Frost ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/29/16	08/12/16	100%
2	Robert Frost ES	FY/19	County Funded	\$118,938	Security Upgrades	Provide and install the following: 1. (51) Fifty-one IP Network Cameras (16- Outside, 35- Inside) 2. 100TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC w	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/04/19	05/31/19	100%
1	Robert Goddard Montessori	FY/18	State & County Funded	\$16,047,000	Systemic Upgrades: HVAC	Replace / upgrade the 1964 106,701 SF school building and 1966 26,930 SF addition mechanical system, composed of two gas fired steam boilers and one chiller.	Substantially Complete	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/22/20	12/29/23	95%
1	Robert Goddard Montessori	FY/26	TBD (currently tracking for other programs)		Renovations: Classroom	Modular Addition	Planning	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>		08/03/26	0%
4	Robert R. Gray ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	12/05/16	12/30/16	100%
4	Robert R. Gray ES	FY/19	County Funded	\$137,763	Security Upgrades	Provide and install the following: 1. (60) Sixty IP Network Cameras (17- Outside, 43- Inside) 2. 100TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	02/04/19	05/31/19	100%
4	Robert R. Gray ES	FY/26	County Funded	\$235,000	Code Corrections	Fire Alarm System Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
5	Rockledge ES	FY/15	County Funded	\$60,000	Systemic Upgrades: Life-Safety	Code Corrections Fire Hydrant Project - This project consists of the replacement of the existing Fire Alarm System to meet current County, State and Federal building codes	Design Procurement	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/19/17	09/30/19	0%
5	Rockledge ES	FY/18	State & County Funded	\$1,431,000	Systemic Upgrades: Misc	Replace the entire 56,252 sf 1994 built-up roof and 8,600 sf 1994 metal roof.	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/22/19	11/20/19	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Rogers Heights ES	FY/21	County Funded	\$525,000	Kitchen & Food Services	Kitchen Renovations	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	06/02/23	08/28/23	100%
4	Rogers Heights ES	FY/23	Operating Funds		Building Repairs: Minor	Flooring Replacement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	07/03/23		
3	Rosa L. Parks ES	FY/20	County Funded	\$154,453	Security Upgrades	Provide and install the following: 1. (64) Forty-nine IP Network Cameras (25- Outside, 39- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/02/20	06/22/20	100%
9	Rosaryville ES	FY/19	County Funded	\$136,219	Security Upgrades	Provide and install the following: 1. (58) Forty-nine IP Network Cameras (15- Outside, 43- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing-Monitor PC	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	02/04/19	05/31/19	100%
8	Samuel Chase ES	FY/26	County Funded	\$184,750	Code Corrections	Fire Alarm System Replacement	Design	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
7	Samuel Massie Academy	FY/21	County Funded	\$202,418	Security Upgrades	Install, program and test Ninety-six IP Network Cameras (32- Outside, 64- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	Contractor Procurement	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
5	Samuel Ogle MS	FY/15	State & County Funded	\$4,776,000	Systemic Upgrades: HVAC	Univents Replacement - This unit ventilator replacement project includes the replacement of approximately 45 univents and 6 convectors in the 1967 building. This project will include new supply and return piping and abatement of existing pipe insulation.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/14/17	10/01/17	100%
5	Samuel Ogle MS	FY/26	County Funded	\$186,600	Athletic Improvements	Gym Bleacher Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
5	Samuel Ogle MS	FY/26	County Funded	\$171,900	Athletic Improvements	Gym Flooring Replacement	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
5	Samuel Ogle MS	FY/26	County Funded	\$90,000	Athletic Improvements	Gym Painting	Contractor Procurement	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	06/22/26	08/14/26	
9	Sasscer Admin Building	FY/21	County Funded	\$255,616	Security Upgrades	SANS server to for sixty-five IP camera systems located throughout the county.	In Construction	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	03/15/21	05/31/21	0%
1	Scotchtown Hills ES	FY/26	State & County Funded	\$2,699,000	Systemic Upgrades: Misc	Replace the 1995 50,153 sf built-up roof.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
4	Seabrook ES	FY/15	County Funded	\$425,000	Code Corrections	Correct Grease Trap Code Violation & General Kitchen Renovation project. Requirements	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/20/16	11/16/16	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
6	Seat Pleasant ES	FY/24	Operating Funds		Abatement	Asbestos Abatement	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/20/24		
3	Sonia Sotomayor MS at Adelphi	FY/26	TBD (currently tracking for other programs)		Other	Major Maintenance Repairs for P3 Schools – Summer 2026  This entry is to track facilities that will be unavailable during Summer 2026 activities due to scheduled maintenance and repairs.	Planning				
2	Springhill Lake ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/29/16	08/17/16	100%
2	Springhill Lake ES	FY/23	Operating Funds		Building Repairs: Minor	Buried Fuel Tank Removal	Contractor Procurement	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	06/30/23		
2	Springhill Lake ES	FY/26	TBD (currently tracking for other programs)		Other	Facility Move/Closure – Summer 2026  This entry is to track facilities that will be unavailable during Summer 2026 activities due to a scheduled move or closure.	Planning	<a href="mailto:kalisa.bell@pgcps.org">kalisa.bell@pgcps.org</a>			
9	Stephen Decatur MS	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	08/05/16	08/20/16	100%
9	Stephen Decatur MS	FY/16	State & County Funded	\$10,501,000	New Schools & Modernizations	Special Education Inclusion Renovation - Renovation of 11,240 net sq. ft. (17,000 GSF) in the southeast corner of the building for the CRI/Regional Program and an added space for the therapy pool to serve the regional students in the area.	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	09/07/20	10/31/23	99%
9	Stephen Decatur MS	FY/16	State & County Funded	\$289,000	Systemic Upgrades: HVAC	Roof Top Units Replacement - The scope of this project will be to remove and replace 7-packaged A/C-Gas Heat Roof Top Units (RTUs) in the 1971 building.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/30/19	08/30/19	100%
9	Stephen Decatur MS	FY/23	County Funded	\$85,290	ADA Upgrades	Lift Upgrade	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_daniel.marks@pgcps.org">pg_daniel.marks@pgcps.org</a>	08/01/23	11/24/23	100%
7	Suitland ES	FY/21	County Funded	\$198,026	Security Upgrades	Install, program and test Ninety-two IP Network Cameras (36- Outside, 56- Inside) with workstation and 43-inch Wall Mounted Live Viewing-Monitor	Contractor Procurement	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>			
7	Suitland HS	FY/14	State & County Funded	\$1,600,000	Renovations: Career Academy	SSR Renovation Business & Finance and Architecture & Design	Substantially Complete	<a href="mailto:cfloek@pgcps.org">cfloek@pgcps.org</a>	06/13/17	09/15/17	99%

**Prince George's County Public Schools  
STATUS OF ACTIVE CAPITAL PROJECTS  
January 2026**

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
7	Suitland HS	FY/15	County Funded	\$45,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	04/01/16	09/21/18	100%
7	Suitland HS	FY/24	State & County Funded	\$101,970,000	New Schools & Modernizations	Complex Replacement	In Construction	<a href="mailto:anoop.gupta@pgcps.org">anoop.gupta@pgcps.org</a>	09/05/22	08/20/27	52%
9	Surrattsville Bus Lot	FY/23	County Funded	\$400,000	Other	Buried Fuel Tank Removal (UST)	In Construction	<a href="mailto:alex.baylor@pgcps.org">alex.baylor@pgcps.org</a>	08/05/24		0%
9	Surrattsville HS	FY/15	State & County Funded	\$2,777,000	Renovations: Career Academy	Secondary School Reform Renovations for the academic academies of Law Education & Public Services and Graphic Arts, Media & Communication	Substantially Complete	<a href="mailto:henry2.lewis@pgcps.org">henry2.lewis@pgcps.org</a>	08/08/17	08/30/18	98%
9	Surrattsville HS	FY/21	Grant Funded (see description)	\$100,000	Athletic Improvements	Stadium Upgrade: Gym Scoreboard and Marquee (per HB101-2019 grant)	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	01/19/22	06/26/25	100%
9	Tanglewood SC	FY/15	County Funded	\$100,000	Systemic Upgrades: Life-Safety	Fire Alarm Project	Contractor Procurement	<a href="mailto:capital.programs@pgcps.org">capital.programs@pgcps.org</a>	06/30/19	08/31/19	0%
8	Tayac ES	FY/16	State & County Funded	\$1,233,000	Exterior Door/Window Upgrades	Exterior Doors and Windows Replacement - This project includes the replacement of 603 windows and 18 doors.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/19/16	09/21/17	100%
8	Tayac ES	FY/18	State & County Funded	\$5,354,000	Systemic Upgrades: HVAC	HVAC - Replace the steam fed heating and ventilating system, and window cooling units, in the 1955 - 1972 portions of the school with a four-pipe heating and cooling system including Replacement of two (2) hot water boilers, is not included in scope.	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/20/20	10/31/20	100%
8	Tayac ES	FY/18	County-Rosecroft Funded	\$34,211	IT Upgrades	Electronic Sign (FY18 Rosecroft Funds \$9,210.52; FY20 Rosecroft Funds \$25,000)	Final Completion (Closeout Approval Requested)	<a href="mailto:pg_rexie.fernando@pgcps.org">pg_rexie.fernando@pgcps.org</a>	02/15/21	06/20/21	100%
8	Tayac ES	FY/20	County Funded	\$126,914	Security Upgrades	Provide and install the following: 1. (48) Forty-eight IP Network Cameras (24- Outside, 24- Inside) 2. 110TB (useable) TB Storage Server RAID 5 3. UPS for Storage Server 4. (1) 43" Wall Mounted Live Viewing-Monitor 5. (1) Live Viewing	Final Completion (Closeout Approval Requested)	<a href="mailto:george2.lacour@pgcps.org">george2.lacour@pgcps.org</a>	07/20/20	11/24/20	100%
4	Templeton ES	FY/15	County Funded	\$45,000	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	06/15/16	08/15/15	100%

Prince George's County Public Schools  
**STATUS OF ACTIVE CAPITAL PROJECTS**  
 January 2026

Board District	School Name	Fiscal Year	Funding Source	Committed Funds	Project Type	Project Description	Current Status/Phase	Project Manager/ POC	Construction Start Date	Substantial Completion Date	Construction Percentage Complete
4	Templeton ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/06/16	08/12/16	100%
6	Thomas G. Pullen Academy	FY/16	State & County Funded	\$3,197,689	Exterior Door/Window Upgrades	Major Repair - Tech Panel Fabrication	Final Completion (Closeout Approval Requested)	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/25/18	08/23/19	100%
6	Thomas G. Pullen Academy	FY/16	State & County Funded	\$2,044,000	Exterior Door/Window Upgrades	Windows Replacement - The scope of this project will be to remove and replace 600 existing windows throughout the entire 1967 building.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/25/18	08/23/19	99%
6	Thomas G. Pullen Academy	FY/26	State & County Funded	\$4,708,000	Systemic Upgrades: Misc	Replace the 2000 89,211 sf built-up roof.	Planning	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>			
4	Thomas Johnson MS	FY/16	State & County Funded	\$6,208,000	Systemic Upgrades: HVAC	Univents Replacement - This project will replace 30 classroom unit ventilators; 3 air handling units and 10 large capacity unit ventilators. It will include unit piping connections to a distance of 10 feet. Equipment will be digitally controlled.	Final Completion (Closeout Approval Requested)	<a href="mailto:ricardo.garcia@pgcps.org">ricardo.garcia@pgcps.org</a>	06/22/18	12/05/25	100%
4	Thomas Johnson MS	FY/25	Grant Funded-ESSER	\$6,830,647	Renovations: Misc	Modular Addition	In Construction	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>		11/25/26	9%
3	Thomas S. Stone ES	FY/16	County Funded	\$36,735	Code Corrections	Upgrade Grease Trap Code Violation Correction Project - This project is required due to non-compliance of existing grease trap to meet current WSSC regulatory code requirements.	Final Completion (Closeout Approval Requested)	<a href="mailto:sunday.owolabi@pgcps.org">sunday.owolabi@pgcps.org</a>	07/14/16	07/28/16	100%
8	Thurgood G. Marshall MS	FY/16	State & County Funded	\$1,011,000	Exterior Door/Window Upgrades	Windows Replacement - The scope of this project will include the removal and replacement of 745 existing windows throughout the entire 1962 building.	Substantially Complete	<a href="mailto:joseph.howell@pgcps.org">joseph.howell@pgcps.org</a>	06/19/18	12/15/18	100%
5	Tulip Grove ES	FY/15	State & County Funded	\$22,902,000	New Schools & Modernizations	Renovation / Addition	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	03/23/17	08/17/18	99%
5	Tulip Grove ES	FY/16	State & County Funded	\$10,582,000	New Schools & Modernizations	Major Renovation and Addition - Major renovation of the existing 23,350 SF with an addition of 41,480 SF to meet modern educational requirements. The facility will be designed with new state-of-the-art, green school features.	Substantially Complete	<a href="mailto:william5.smith@pgcps.org">william5.smith@pgcps.org</a>	06/20/17	12/22/18	99%
